

City of Oronoco

Home of Downtown Oronoco Gold Rush



January 12, 2023

**Reference: Resident Construction Status Update No. 17:
Oronoco Wastewater Treatment, Sewer Collection System & Water Distribution Project**

Review of recent construction:

Over the past month, Fitzgerald Excavating & Trucking and been working when the weather was good and outside of the holiday weeks. During this time, the contractor installed gravity sanitary sewer piping and associated structures in Riverwood Hills Park and in Memorial Park. Fitzgerald Excavating crews also completed installation of effluent outfall piping between the river and 100th St NW / CR 112.

Work planned over the next few weeks and associated traffic, roadway access, and service impacts are summarized below. Note: The tentative work schedule provided by the contractor is subject to weather conditions and construction progress and may change without notice. See attached figure for additional information.

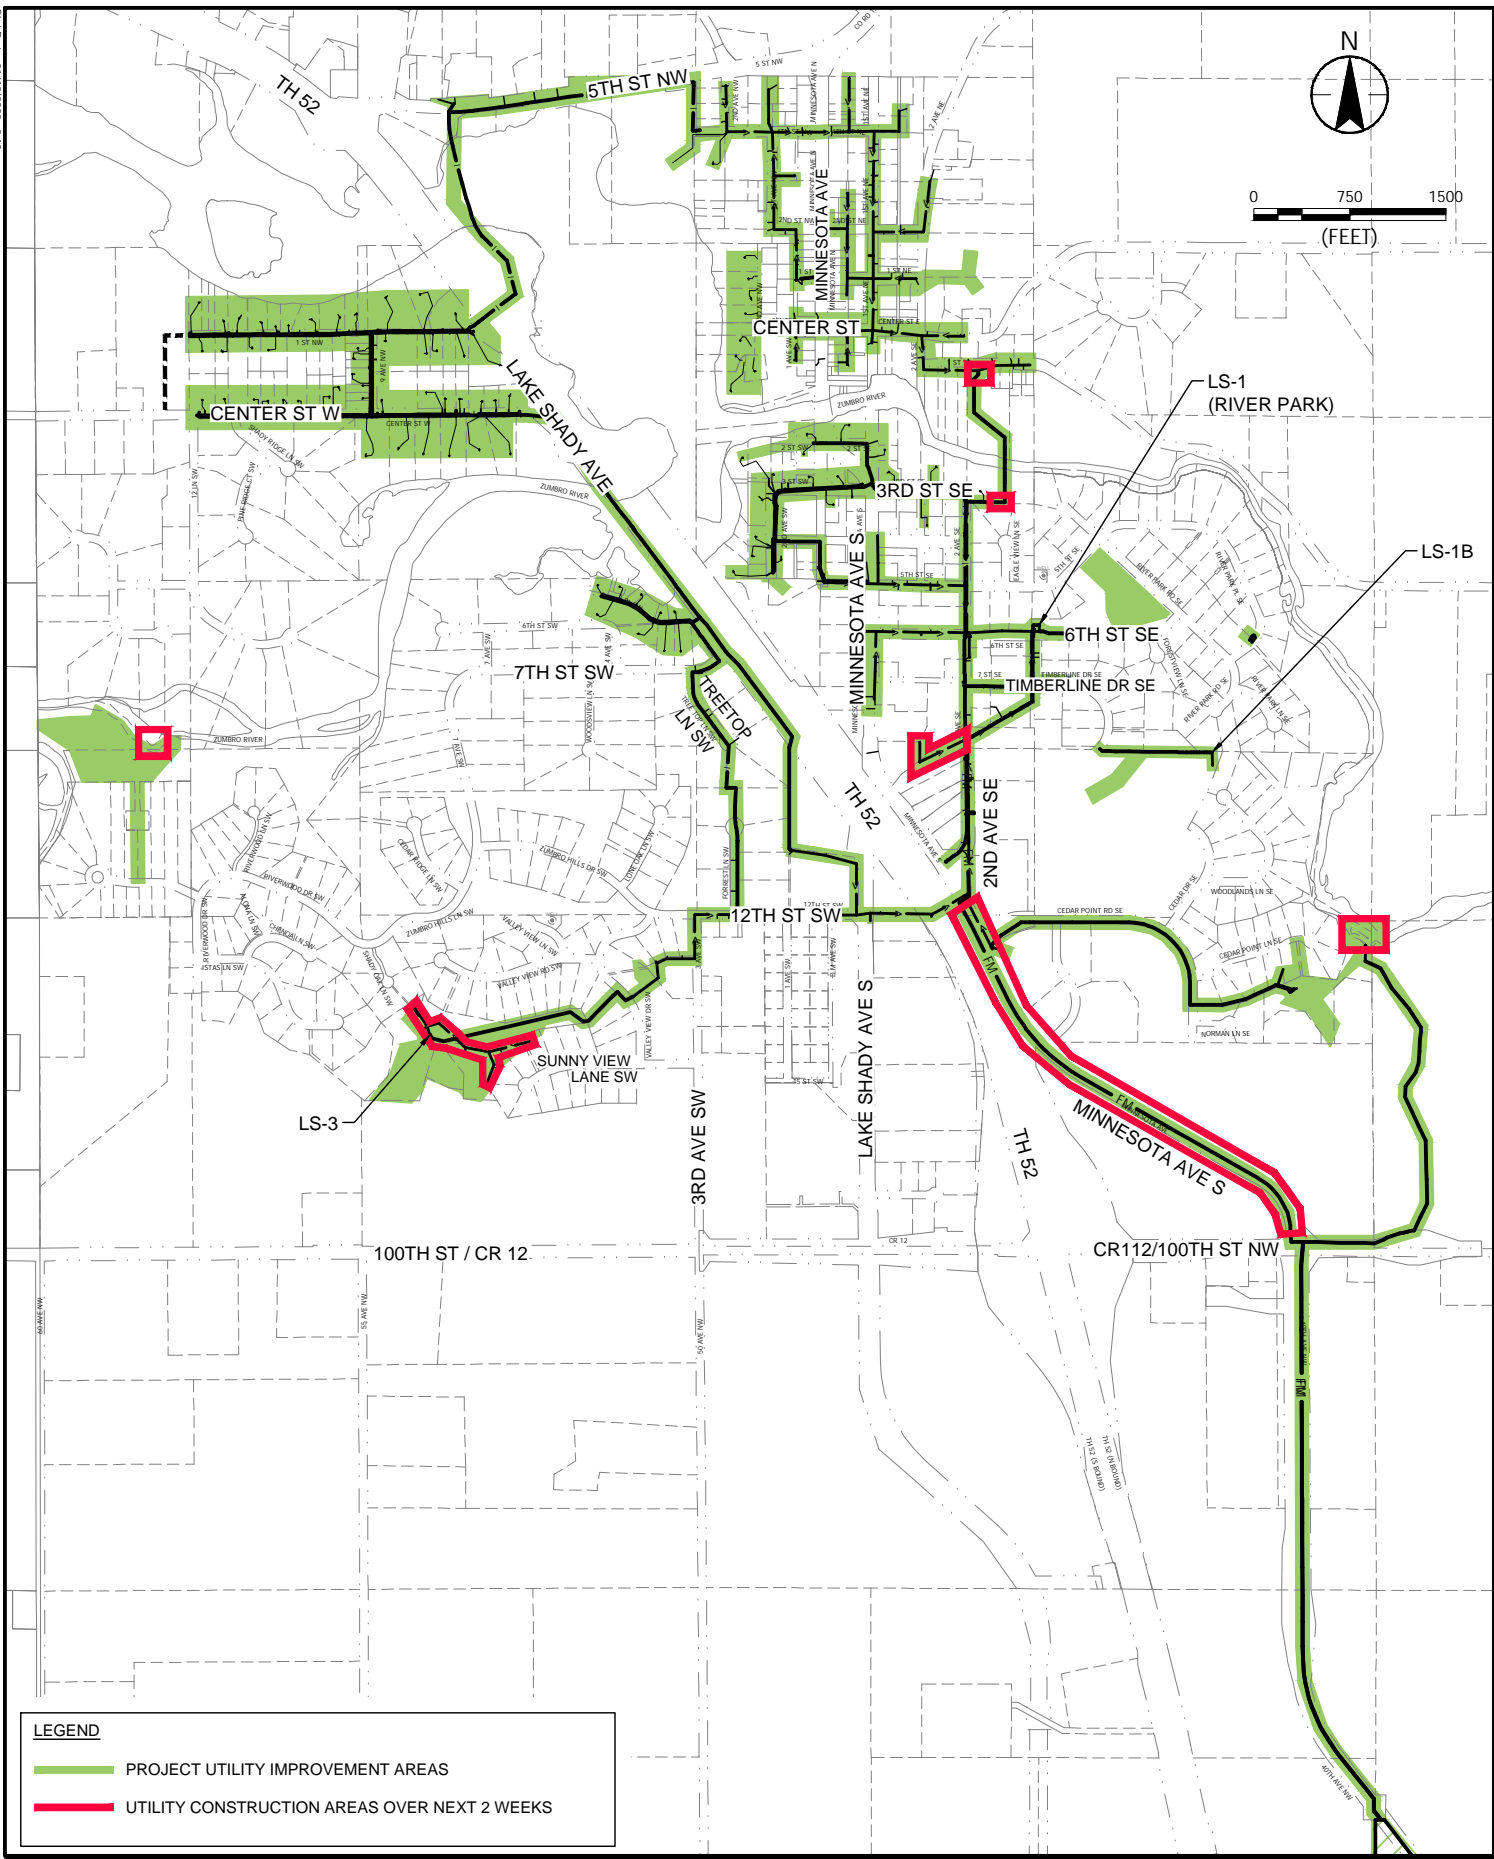

1. Construction of utilities directly impacting existing roadway pavements has been suspended for this winter construction season. Construction of utility improvements outside of paved roadways will continue throughout the winter months. All roadway and driveways disturbed by construction to date have been reconstructed through bituminous base.
2. Fitzgerald crews will continue work in Riverwood Hills Park in southwest Oronoco. This work involves installation of gravity sanitary sewer and manhole structures.
3. Fitzgerald crews will install sanitary sewer force main piping in the west ditch of Minnesota Ave S, between 100th St NW / CR 112 and 2nd Ave SE. Minimal impacts to traffic are expected, please exercise caution driving through this area.
4. Fitzgerald crews will work on installation of sanitary pipe and structures in the field west of 2nd Ave SE and north of Advanced Building Center.
5. Riverbank stabilization improvements will begin at the Zumbro river located east of Cedar Woodlands 2nd Subdivision.
6. A crew will repair minor erosion a one spot on the riverbank stabilization at Riverbend Estates.
7. A crew from Fitzgerald Excavating will be working in Garden Park at LS-2. No impacts to traffic are expected.
8. A crew from Fitzgerald Excavating will install forcemain pipe fittings and a valve east of the intersection of 3rd Street SE at 2nd Avenue SE.
9. Continued material deliveries to construction work areas will periodically occur. Expect truck traffic and periodic delays as materials are unloaded.
10. School Bus Coordination – An informational letter was sent out on August 25, 2022. Questions about Rochester school bus routes and stops can be emailed to Michael Pearse at michael.pearse@firstgroup.com. Questions about Pine Island school bus routes and stops can be emailed to Lisa Swanson at lswanson@pineisland.k12.mn.us.

The City and construction team recognizes this project will temporarily impact and inconvenience many residents during the construction of the critically important sewer and water improvements. Construction traffic, access constraints & delays, use of alternate access routes, dust, and muddy streets are all unfortunate realities associated with this type of construction. The City of Oronoco and its Contractors sincerely appreciate resident cooperation and your patience as we work together to complete this project.

Resident construction status updates will be posted on the City's website, emailed directly to residents who have provided their email address to the City, and printed for pickup at temporary mailbox stands located in construction areas. To facilitate enhanced dissemination of the update to residents, we ask that residents sign up for email updates by sending an email to Oronococonstruction@gmail.com. In addition to this update, the City has prepared a Frequently Asked Questions (FAQ) document that addresses common resident construction related questions and is also available on the City's website. Questions about the contents of the construction status update or about the project in general can be directed to the City's Engineer Joe Palen at either 507.529.6036 or joseph.palen@stantec.com.

Questions or concerns about construction activities, driveway or roadway access, service interruptions or safety can be directed to Fitzgerald Excavating and Trucking Staff: Project Manager Gary Richter - (507) 208-0473 or Project Foreman Joe Fogarty (507) 517-8512.

Print Date: 01/11/2023 2:21 PM
User: ADJ.Dwyer
Figure Area: 193804990
Xref: 193804990_contract.dwg
Xref: 193804990_SSS_193804990.dwg



LEGEND

- PROJECT UTILITY IMPROVEMENT AREAS
- UTILITY CONSTRUCTION AREAS OVER NEXT 2 WEEKS

CITY OF ORONOCO UTILITY CONSTRUCTION IMPACTS
WASTEWATER COLLECTION SYSTEM & WATER DISTRIBUTION IMPROVEMENTS



3800 Highway 52 N, Ste 130
Rochester, MN 55901
www.stantec.com
