

City of Oronoco

Home of Downtown Oronoco Gold Rush



April 20, 2023

**Reference: Resident Construction Status Update No. 21:
Oronoco Wastewater Treatment, Sewer Collection System & Water Distribution Project**

Review of recent construction:

Over the last few weeks, Oronoco's contractor (Fitzgerald Excavating & Trucking) has been working when the weather and conditions permit. During this time, the contractor has:

- Completed installation of forcemain piping between Lift Station 4 and Cedar Point Ln SE.
- Installed forcemain piping and services along 2nd Street SE to 3rd Street SE.
- Completed miscellaneous utility pressure tests.
- Worked in multiple areas on fine grading in preparation for turf establishment.

Work planned over the next two weeks and associated traffic, roadway access, and service impacts are summarized below. Note: The tentative work schedule provided by the contractor is subject to weather conditions and construction progress and may change without notice. See attached figure for additional information about where work is tentatively planned over the next two weeks.

1. Fitzgerald crews will begin installation watermain and sanitary sewer forcemain piping along 1st Place SW. The contractor will begin work on the west end of 1st Place SW and will incrementally complete utility improvements to limit impacts to property owner assess. Please note that access to 1st Place SW cannot be guaranteed from 7 AM to 7 PM (Monday through Saturday) adjacent to and west of construction activities. Please plan to park vehicles at a location out of the construction area if you need to leave home during these times or if heavy rain is forecast. The contractor will work directly with property owners to facilitate access when feasible and will maintain access to roadway and driveways outside of construction hours and all day on Sunday unless precluded by certain construction activities or wet weather conditions.
2. A Fitzgerald crew will be installing forcemain service piping along 2nd Street SE. The contractor will work directly with adjacent impacted property owners to coordinate access to their properties. Please be patient and anticipate periodic delays and access interruptions.
3. Within the next two weeks, a crew from Fitzgerald Excavating will begin installing sanitary sewer main along 3rd Street SE. Access to 3rd Street SE may be restricted between 7:00 AM and 7:00 PM (Monday through Saturday). Please plan to park vehicles at a location out of the construction area if you need to leave home during these times or if heavy rain is forecast. The contractor will maintain access to roadway and driveways outside of construction hours and all day on Sunday unless precluded by certain construction activities or wet weather conditions.
4. A crew from Fitzgerald Excavating will be working in Riverwood Hills Park to install sanitary sewer main and water service piping to LS-3. Please exercise caution around construction activities, avoid areas near active construction, and provide adult supervision for children playing in areas of the park not impacted by construction.
5. Mail Service, Garbage Service and UPS / FedEx deliveries within areas impacted directly by construction.
 - Beginning next week, existing mailboxes on 1st Place SE will be temporarily out of service. A bank of temporary mailboxes for these residents will be located on 7th Street SW near 1st Place SW intersection.

- Beginning in the next week or two, existing mailboxes on 3rd Street SE will be temporarily out of service. A bank of temporary mailboxes for these residents will be located on 2nd Avenue SE near 3rd Street SE.
 - Deliveries from UPS / Fed Ex to properties adjacent to the construction zone cannot be guaranteed as access to the roadway will frequently be limited. Please make other arrangements for deliveries or schedule to pick up packages directly from the carrier.
 - Garbage Service on 1st Place SE and 3rd Street SE will be facilitated by the contractor. Please put your garbage out as normal and the contractor will work with the garbage collectors and see that service is provided.
6. The contractor will continue fine grading activities and preparations for turf establishment within ditches and boulevards impacted by past utility construction. Minimal impact to local traffic is expected.
 7. Continued material deliveries to construction work areas will periodically occur. Expect truck traffic and periodic delays as materials are unloaded.
 8. School Bus Coordination: No major impacts to school bus routes or pick up locations are anticipated over the next few weeks. Questions about Rochester school bus routes and stops can be emailed to Michael Pearse at michael.pearse@firstgroup.com. Questions about Pine Island school bus routes and stops can be emailed to Lisa Swanson at lswanson@pineisland.k12.mn.us.

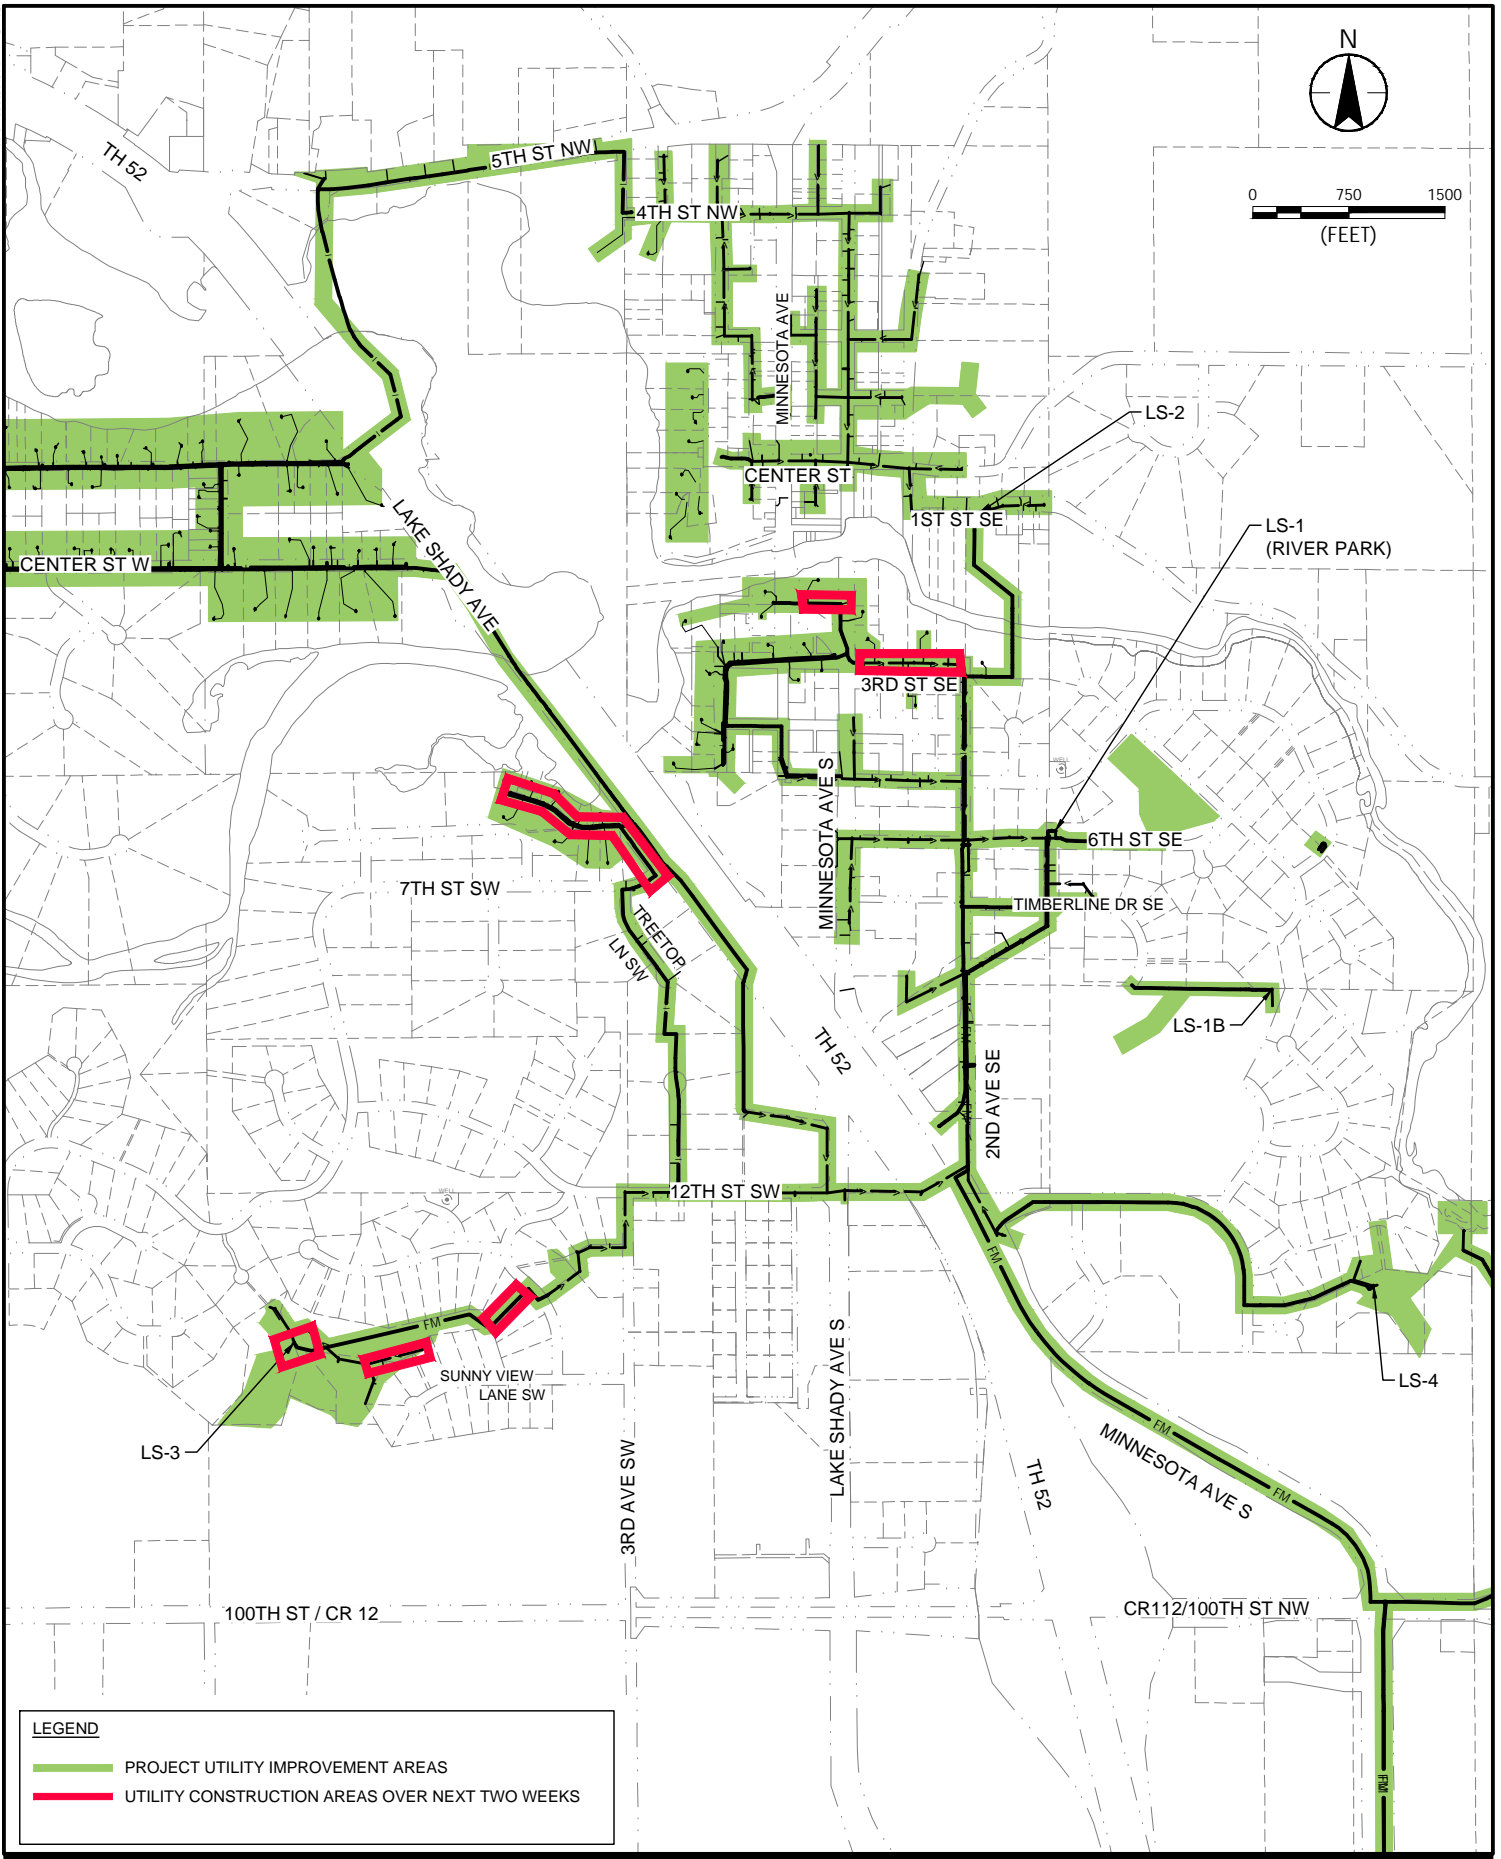

A Public Open House events are planned for May 22 and May 23, 2023 to provide residents with the opportunity to learn more about project construction planned for 2023, discuss anticipated construction impacts and the anticipated construction schedule. Additional information regarding the Public Open House and guidance on sanitary sewer and water service connections is forthcoming.

The City and construction team recognizes this project will temporarily impact and inconvenience many residents during the construction of the critically important sewer and water improvements. Construction traffic, access constraints & delays, use of alternate access routes, dust, and muddy streets are all unfortunate realities associated with this type of construction. The City of Oronoco and its Contractors sincerely appreciate resident cooperation and your patience as we work together to complete this project.

Resident construction status updates will be posted on the City's website, emailed directly to residents who have provided their email address to the City, and printed for pickup at temporary mailbox stands located in construction areas. To facilitate enhanced dissemination of the update to residents, we ask that residents sign up for email updates by sending an email to Oronococonstruction@gmail.com. In addition to this update, the City has prepared a Frequently Asked Questions (FAQ) document that addresses common resident construction related questions and is also available on the City's website. Questions about the contents of the construction status update or about the project in general can be directed to the City's Engineer Joe Palen at either 507.529.6036 or joseph.palen@stantec.com.

Questions or concerns about construction activities, driveway or roadway access, service interruptions or safety can be directed to Fitzgerald Excavating and Trucking Staff: Project Manager Gary Richter - (507) 208-0473 or Project Foreman Joe Fogarty (507) 517-8512.

Plot Date: 04/19/2023 12:28pm ADX.Dwg, Figure Area: 193804990, Figure Content Impact: dng
Xref: 193804990, connectivity, 193804990_SSS, 193804990_Aerial



LEGEND

- PROJECT UTILITY IMPROVEMENT AREAS
- UTILITY CONSTRUCTION AREAS OVER NEXT TWO WEEKS

CITY OF ORONOCO

UTILITY CONSTRUCTION IMPACTS



WASTEWATER COLLECTION SYSTEM & WATER DISTRIBUTION IMPROVEMENTS

3800 Highway 52 N, Ste 130
Rochester, MN 55901
www.stantec.com

DATE 4/20/2023

PROJ. NO. 193804990
